


## **Product Description**

# Heya-3S03



QUOTATION SHEET							
Heya-3S03							
NO	ITEM	DESCRIPTION	UNIT	THEORY QTY	LOSS RATE	UNIT	ACTUAL QTY
<b>Frame System</b>							
1	Steel structure		m²	107.00	1.00	T	4.28
2	Fittings		set	107.00	1.00	m²	107.00
<b>Wall System</b>							
3	External wall foamed cement board	610*2270*130mm	m²	127.00	1.10	pc	101.00
4	Internal wall foamed cement board	610*2270*130mm	m²	100.00	1.10	pc	80.00
<b>Roof System</b>							
5	Roof panel	75mm EPS sandwich panel	m	239.20	1.10	m	263.12
<b>Door &amp; Window System</b>							
7	PVC window		m²	12.54	1.00	m²	12.54
8	PVC door		m²	14.40	1.00	m²	14.40
<b>Decoration System</b>							
9	Ceiling	gypsum board,600*600mm 10pcs/pack	m²	107.00	1.10	pack	12.00
10	Floor tile	ceramic tile 600*600mm 10pcs/pack	m²	107.00	1.10	pack	12.00
11	Internal Putty	Brand:Nippon 15kgs/bag	m²	327.00	1.10	bag	24.00
12	Internal wall coating	white,18L/bucket	m²	327.00	1.10	bucket	4.00
13	External wall coating	16L bucket	m²	127.00	1.10	bucket	2.00
<b>Water&amp;Electric System</b>							
14	Drain pipes_gutter		m	43.00	1.00	m	43.00
15	Water Pipes	inlet & outlet pipes	m²	107.00	1.00	m²	107.00
16	Electric system	Include weak current,exclude socket/switch/light,etc	m²	107.00	1.00	m²	107.00
<b>Hardware Accessories System</b>							
17	Hardware Accessories System		m²	107.00	1.00	m²	107.00
<b>Fitting facilities</b>							
18	Toilet		pc	0.00	1.00	pc	0.00
19	Basin		pc	0.00	1.00	pc	0.00
20	Shower		pc	0.00	1.00	pc	0.00
21	Kitchen Cabinet		m	0.00	1.00	m	0.00
<b>Inland Transportation</b>							
22	Inland cost	loading fee,truck transport,custom declare,post charges,etc.	nos				1.00
<b>TOTAL PRICE (FOB Qiongdao)</b>				<b>\$18,484.93</b>			

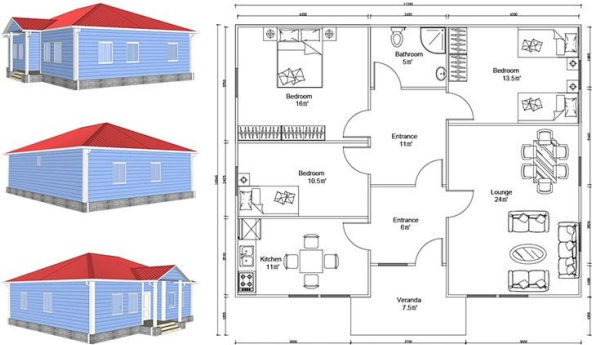
